







City of Phoenix
STREET TRANSPORTATION DEPARTMENT

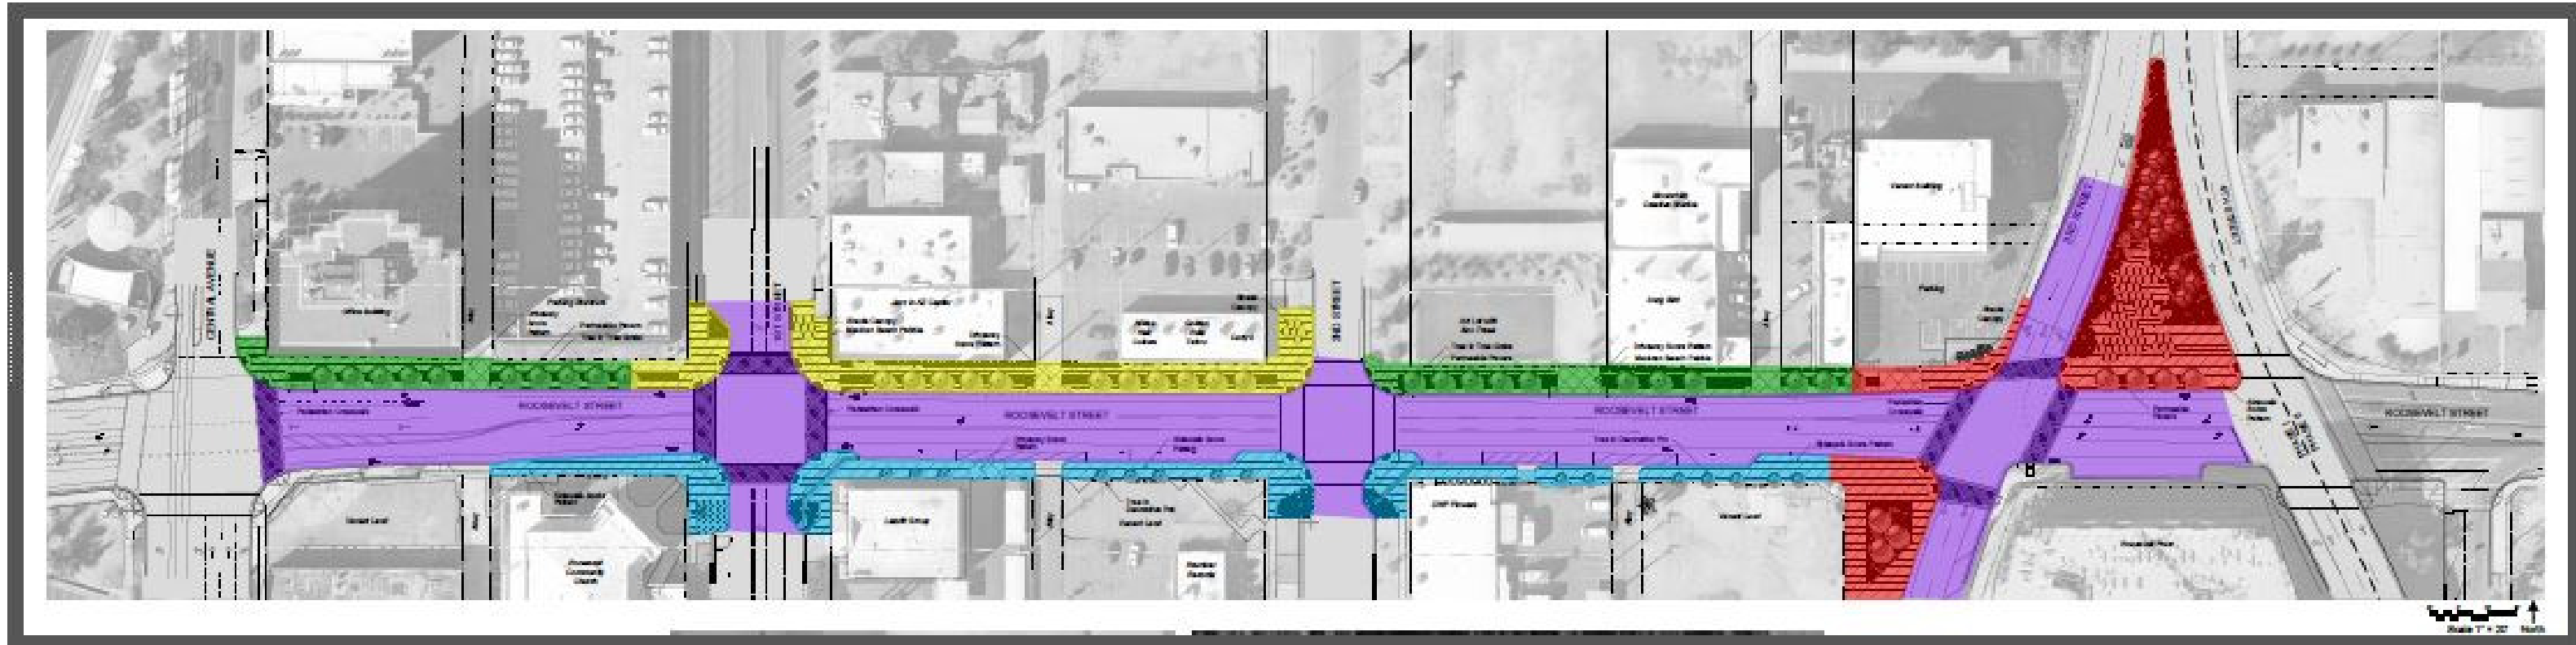

**Roosevelt Street Improvement Project: Central Avenue to 4th Street
Anticipated Construction Phasing**

- 
South side of Roosevelt
 Blue: remove existing sidewalk and driveways; install underground utilities including traffic signal and street light conduit, and irrigation pipe; install new sidewalk, driveways, curb and gutter from the alley east of Central Avenue to west side of 3rd Street.
Approximate Duration: June 2014 to the end of August 2014
- 
North side of Roosevelt
 Yellow and Green: remove existing sidewalk, driveways, curb and gutter; install underground utilities including traffic signal and street light conduit, and irrigation pipe; install storm drain, catch basins, water main; install new sidewalk, driveways, curb and gutter; shade structure footing, pavers, and grates from the east side of Central Avenue to the west side of 3rd Street. Construction will begin on the west side of 1st Street to the west side of 2nd Street. (Yellow) The contractor will then continue construction activities on the east side of 2nd Street to the west side of 3rd Street. Followed by construction activities on the east side of Central Avenue to the west side of 1st Street. (Green)
Approximate Duration: September 2014 to middle of January 2015
- 
Remaining areas of Roosevelt
 Red and Purple: remove existing sidewalk, driveways, curb and gutter; install underground utilities including traffic signal and street light conduit, and irrigation pipe; install storm drain, catch basins, water main; install new sidewalk, driveways, curb and gutter; shade structure footings, pavers, and grates at 3rd and 4th Streets. (Red) Roadway grading and paving; utility adjustments and new striping throughout project limits. (Purple)

Complete remaining landscaping including new tree installation, pots and other pedestrian features throughout project limits.

Approximate Duration: February 2015 to the end of March 2015
